

**SAFETY  
MUSIC & ART  
ATHLETICS  
RENOVATION  
TECHNOLOGY**



March 20, 2025

# **BOND OVERSIGHT COMMITTEE**

Data through December 31, 2024// **FY25 Q2**

# Facilities



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

Facilities

# Quarterly Highlights



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

# Quarterly Highlights

**SAFETY  
MUSIC & ART  
ATHLETICS  
RENOVATION  
TECHNOLOGY**



JAMES S. RICKARDS MS



MCARTHUR HS




CORAL SPRINGS HS

- ▶ This quarter, the number of projects in **construction closeout** went up by **17** to **169 in total**.
  - ▶ Reflects a Year-to-Year difference of **80** projects moved into construction closeout in the last year.

- ▶ **Four Ribbon-Cutting ceremonies** took place this quarter.
- ▶ We continued the school year by visiting schools with construction underway and completed **over 29 school visits this quarter**.

# Quarterly Highlights


## PRIMARY RENOVATION PROCESS CHART

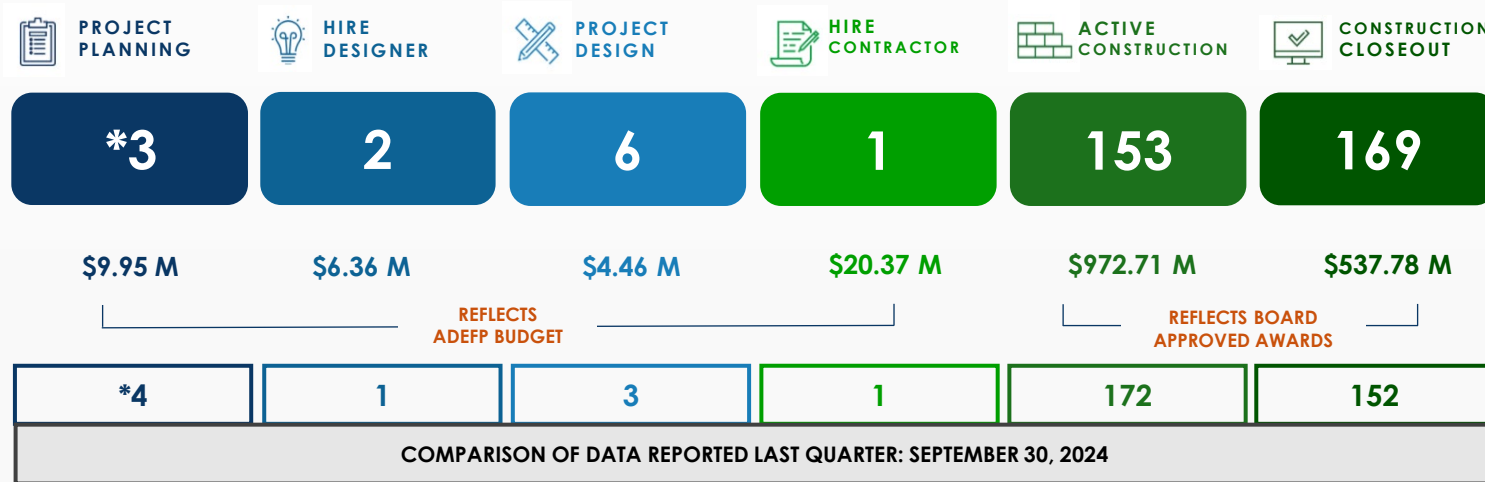

Disclaimer: Some schools have multiple Primary Renovations projects in different phases.

\* Projects are on hold. Preliminary planning will initiate once further decisions are made.

# Quarterly Highlights

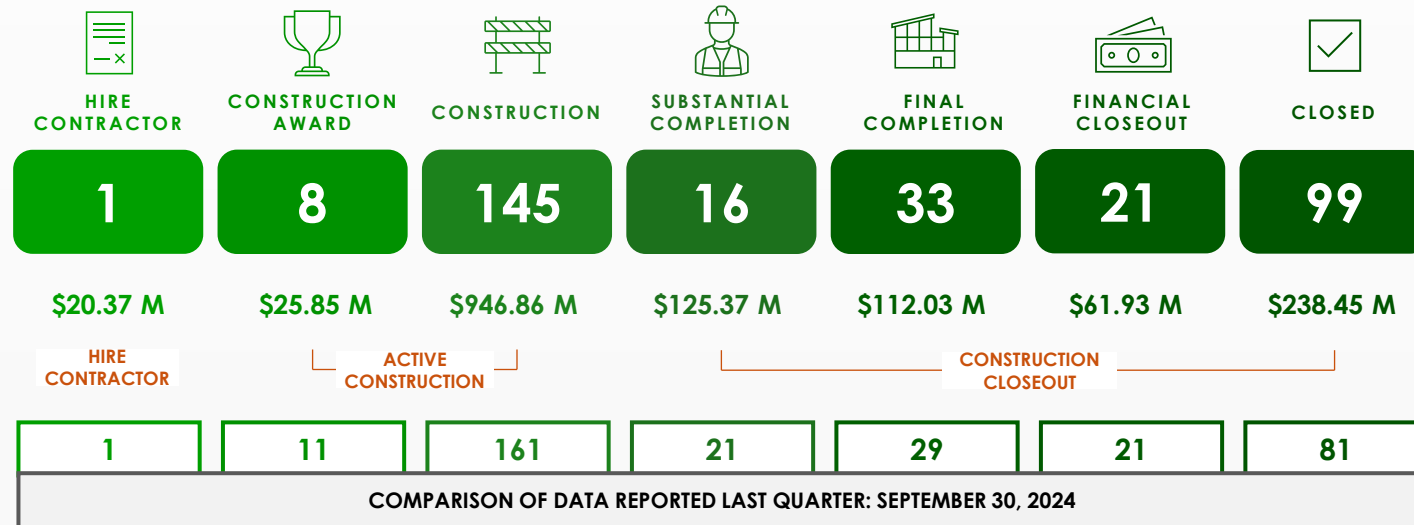

Disclaimer: Some schools have multiple Primary Renovations projects in different phases.

\*\* Reflects Board Approved Awards

Facilities

# Status & Timeframes of Remaining Safety and Security Projects



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

# Safety Status



|                | Planning | Design | Hire Contractor | Construction | Complete/<br>Closeout | Total |
|----------------|----------|--------|-----------------|--------------|-----------------------|-------|
| Fire Alarm     | 1        | 1      | 1               | 67           | 28                    | 97    |
| Fire Sprinkler | 1        | 1      | 1               | 56           | 32                    | 90    |

The Fire Alarm count has been reduced by one because the scope was only a panel replacement which was assessed by the Engineer as being in good condition.

The Fire Sprinkler count has been reduced by one because the scope had been completed as part of a previous project.

**Single Point of Entry (SPE) projects where the security scope of work in the SMART program. All SPE projects were completed and deemed fully operational by July of 2019.**

# Fire Alarm Flags

| SCHOOL                             | % COMPLETE | STATUS                                                                                                                                                                                                                                                                                                                                                                                     |
|------------------------------------|------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Attucks MS                         | 95         | All fire alarm devices have been installed. The contractor is finalizing the installation and wiring of facts and voice panels.                                                                                                                                                                                                                                                            |
| Country Isles ES                   | 95         | Fire Alarm devices were added during final inspection, the contractor is preparing a change order. Additional devices were added during inspection. Contractor has proceeded with the work. Will require revised shop drawings to pass final inspections. Pending revised shop drawings and calculations approval.                                                                         |
| Deerfield Park ES                  | 95         | Fire alarm devices electrical wiring were installed per approved shop drawings, specifications and code. Building official has failed the electrical finals requesting all the new wiring be pulled and updated.                                                                                                                                                                           |
| Driftwood MS                       | 92         | Fire alarm work is ongoing. Scope of work is only the Smoke Duct Detector Test Stations. The Shop Drawing have been approved. A change order is forthcoming for this work. Contractor refuses to sign CORP approved change orders. BCPS Legal has been engaged as there is ongoing litigation with the Contractor.                                                                         |
| Griffin ES                         | 100        | The 110b substantial completion has been submitted to the Building Department. Final NFPA 72 is passed. Structural punch list items are on going. GC working with engineer to certify existing conditions. An ASI is currently in the Building Department for review.                                                                                                                      |
| Hallandale Magnet HS               | 92         | Roughing in 120 additional fire alarm devices.                                                                                                                                                                                                                                                                                                                                             |
| Maplewood ES                       | 96         | FA work is 95% complete. Change Orders for additional devices for the FA, requested a final inspection, delaying the completion of the FA. This was missed by the Shop Drawing code compliance review. In the process of certifying, programming and recalling failed inspections. BCPS Legal has been engaged as there is ongoing litigation with the Contractor.                         |
| Millennium 6-12 Collegiate Academy | 99         | Additional fire alarm devices were added during final inspection. Installation of the new devices is ongoing.                                                                                                                                                                                                                                                                              |
| Northeast HS                       | 92         | Fire alarm installation is complete. Contractor is calling final inspections.                                                                                                                                                                                                                                                                                                              |
| Oakridge ES                        | 93         | FA work is ongoing. Contractor has delayed the project and has been put on Notice. Change order under review for additional fire alarm devices. Contractor will not proceed with the work until change order is executed. Another Cure Notice has been sent to the Contractor regarding the ongoing issues.                                                                                |
| Pompano Beach MS                   | 100        | Fire alarm certification has passed. The 110b has been submitted to the Building Department. The fire alarm certification has been completed. We are currently awaiting ASI approval before scheduling the final inspections and submitting the 110B. The punch list items are in progress to be resolved and the Contractor is working thru Final Inspections in order to achieve a 110b. |
| Ramblewood MS                      | 98         | Contractor scope of work is complete, Fire Alarm certification is in progress. Fire alarm certification has been requested for two additional devices installed. The 209 final completion is in progress.                                                                                                                                                                                  |
| Riverglades ES                     | 92         | Contractor has demobilized and refuses to continue work until progress payment is made. A Notice to Cure has been issued. Fire alarm contractor has remobilized. Approximately 2 months worth of work and testing to compete. BCPS Legal has been engaged, and the situation is under review.                                                                                              |

# Fire Alarm Flags

| SCHOOL                   | % COMPLETE | STATUS                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
|--------------------------|------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Sandpiper ES             | 93         | 110b submitted to the Building Department. Pending fire alarm annunciator final. Additional devices are being requested by the Fire Department; PO has been issued to BASS. This project is under review by BCPS Senior Leadership.                                                                                                                                                                                                                                                                                                                                                                                                                          |
| Sea Castle ES            | 99         | Fire alarm change order was approved. Work is completed. Final inspections and testing is on going. During the functional test 19 additional devices were requested. A CCD is in process. The A/E has been non-responsive on the and has been issued a Cure Notice. BCPS Legal has been involved.                                                                                                                                                                                                                                                                                                                                                            |
| Sheridan Hills ES        | 97         | Additional fire alarm devices were added during final inspection. Installation is complete. Contractor calling for final inspections.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |
| Seagull Alternative HS   | 93         | Fire alarm is complete. Final inspection, testing and switch over remain. To correct previous BOC comments, changes on fire alarm are because of 1) single point of entry added after design was completed and 2) added devices in portals located approved, adjacent school but are being used by Seagull. Devices have been added to the portables; however, a comment from the Building Department is being addressed in order to begin testing and certification of the system. The shop drawings are being revised to accommodate new comments. ASIs have been approved and Change Orders are in progress. A Notice of Concern has been sent to the GC. |
| Tedder ES                | 88         | All devices installed. Bass working on the programming. FA testing/troubleshooting ongoing.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
| The Quest Center         | 98         | FA installation completed. All additional fire alarm devices have been installed. Fire alarm has been certified. Preparing 110b for submission to the Building Department. Additional fire alarm devices are required by the Fire Department. Contractor is pricing change order. Contractor has submitted the change order for additional devices and is under review by the PMOR. Contractor will not proceed with the work until change order is executed. Updated drawings have been submitted and are under review.                                                                                                                                     |
| Tropical ES              | 88         | This scope of work is behind schedule. The contractor is in the process of terminating the subcontractor due to lack of performance. Installation is ongoing - currently 50% complete.                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
| Virginia Shuman Young ES | 91         | Fire Alarm shop drawings were approved. Additional fire alarm devices were added. Work has begun and they are currently 30% complete.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |
| Walker ES                | 98         | Project was delayed due to the added scope of tying in the Old Dillard Building FA to the new FA system. Roofing, mechanical, and fire alarm work is ongoing. No trade has been completely finalized; the GC is not moving forward with the work. A CCD for the additional Old Dillard Museum is in process A notice to cure will be issued. A CCD and Notice to Cure have been issued.                                                                                                                                                                                                                                                                      |

Facilities

# Primary Renovations Projects Schedule Updates



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES




BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

# Schedule Milestones

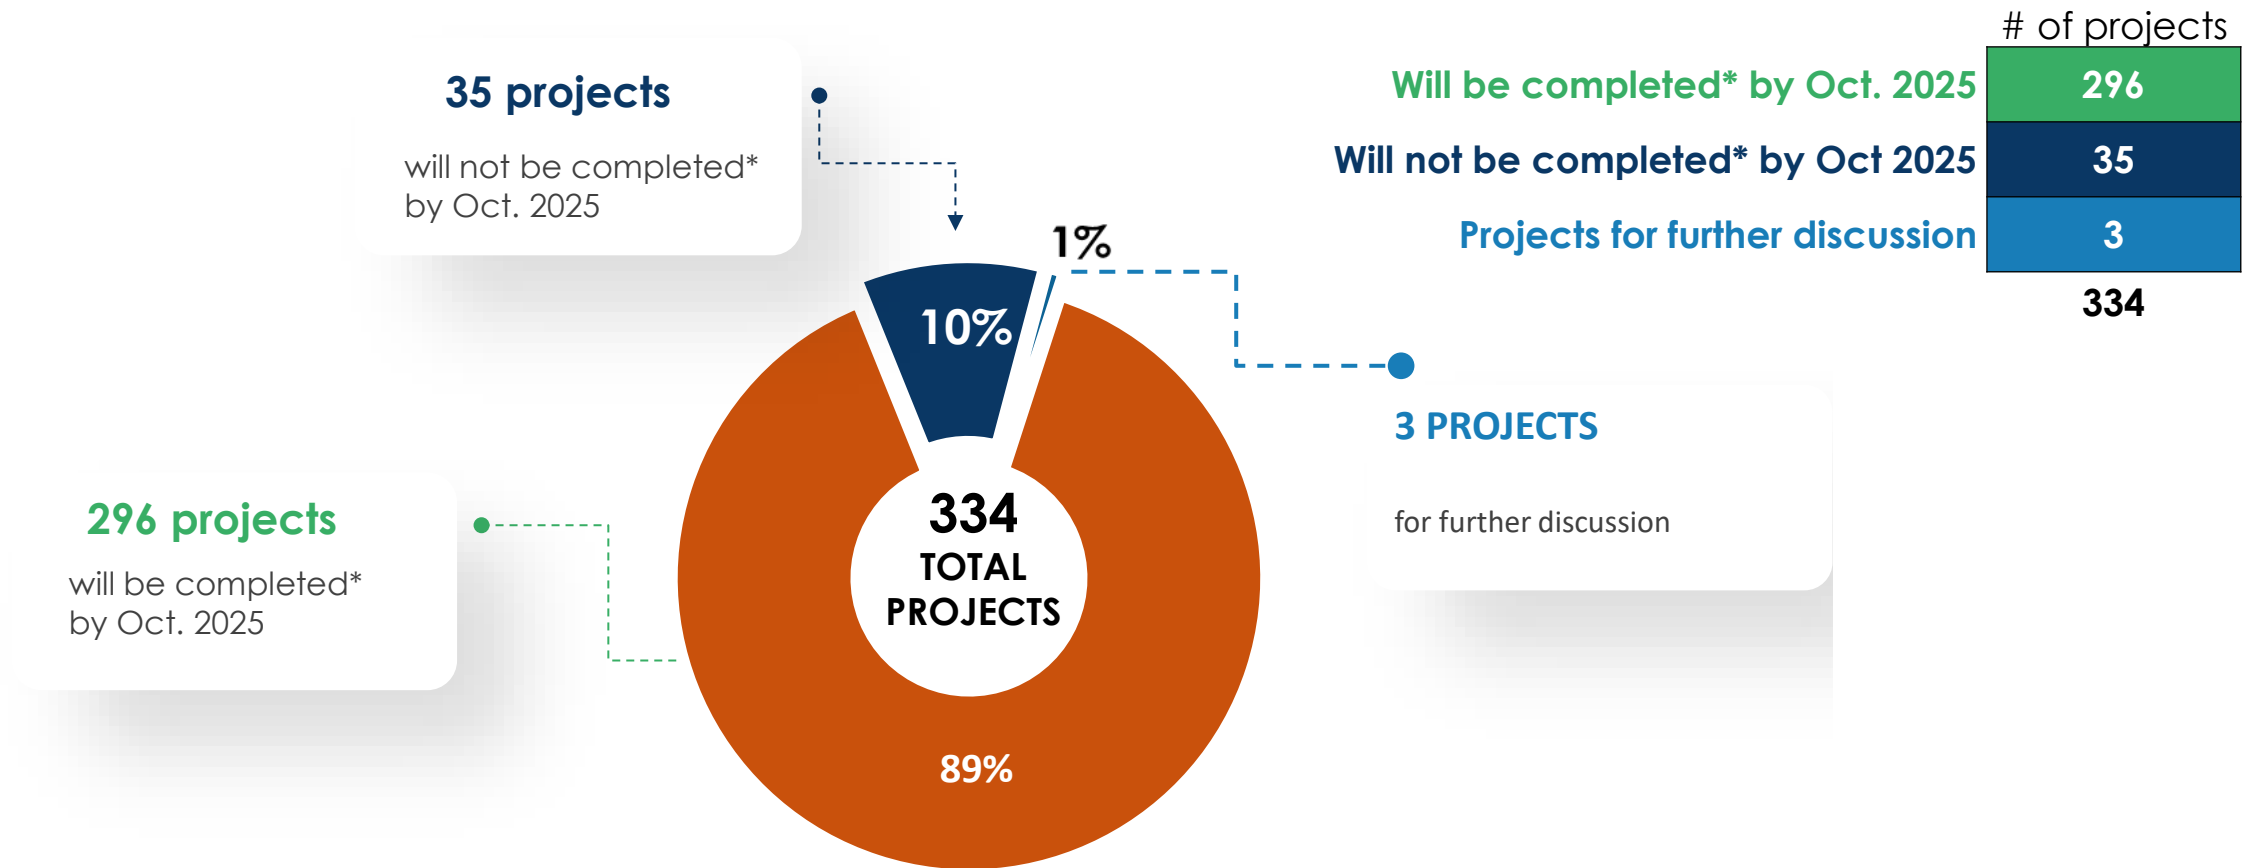

*\*Completed projects are defined as projects where the space has obtained occupancy and is being utilized for its intended use.*

# Schedule Milestones

The schools listed below are not anticipated to be completed\* by October 2025.

| Project Number | Project Name                      | Delay Event                                                                                                                                                                                                          | *Substantial Completion |
|----------------|-----------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| P.002061       | Dania ES                          | District's delay in deciding whether Building 2 would be demolished or renovated.                                                                                                                                    | 11/1/2025               |
| P.001729-ELE   | Plantation MS                     | Original GOB contractor was terminated for non-performance. The remaining scope was broken out into design-build carve out projects and were recently awarded.                                                       | 12/1/2025               |
| P.002860       | Morrow ES                         | Delayed awaiting approval to carve out project and funding for the project.                                                                                                                                          | 12/8/2025               |
| P.002000       | Virginia Shuman Young ES          | Two large mechanical change orders for roof top units and classroom ductwork. Fire alarm permit review delays due to the contractor.                                                                                 | 12/15/2025              |
| P.002142       | Deerfield Beach MS                | When it was decided to carve out the roof, the A/E firm refused to proceed until a contract for the roofing was in place                                                                                             | 12/15/2025              |
| P.001903-ADA   | North Lauderdale ES               | The project was carved out, and the proposals came in too high. Therefore, it was decided that the architectural design would be done by the pre-construction team. A commitment was made to secure an MEP contract. | 12/20/2025              |
| P.001710       | New River MS                      | Litigation issues have delayed the project.                                                                                                                                                                          | 12/30/2025              |
| P.001951       | Seagull Alternative HS            | Additional fire alarm devices were added during final inspections. GC delays, unforeseen conditions, and consultant delays                                                                                           | 12/31/2025              |
| P.001711       | Whiddon Rogers Educational Center | Contractor delays, lack of swing space has pushed the installation of AHUs to summer causing delays.                                                                                                                 | 12/31/2025              |
| P.001979       | Coral Springs MS                  | Unforeseen conditions, roof deck replacement which has caused issues with the remaining work.                                                                                                                        | 12/31/2025              |
| P.002148       | Monarch HS                        | A/E and Contractor delays.                                                                                                                                                                                           | 12/31/2025              |

# Schedule Milestones

The schools listed below are not anticipated to be completed\* by October 2025.

| Project Number | Project Name                | Delay Event                                                                                                                                                                                                                                                                                          | *Substantial Completion |
|----------------|-----------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| P.002091       | Pompano Beach HS            | A/E and contractor delays.                                                                                                                                                                                                                                                                           | 12/31/2025              |
| P.001954       | McArthur HS                 | Change in the delivery method                                                                                                                                                                                                                                                                        | 1/1/2026                |
| P.000817       | Marjory Stoneman Douglas HS | Change in the delivery method                                                                                                                                                                                                                                                                        | 1/1/2026                |
| P.001916       | Plantation HS               | QSEC deemed contractor did not meet the minimum qualifications for recommendation of award and therefore rejected the bid, recommending to the School Board that the project be re-bid. The District staff did not proceed with that recommendation. Contractor protested. Rebid.                    | 1/1/2026                |
| P.002132       | Sanders Park ES             | A/E and contractor delays.                                                                                                                                                                                                                                                                           | 1/1/2026                |
| P.001836       | Margate MS                  | Change in the delivery method                                                                                                                                                                                                                                                                        | 1/5/2026                |
| P.001796-HVC   | Atlantic West ES            | The project was carved out, and it took a long time to get quotes from CSMPs for a design-build. We received some proposals, but the cost would be double. We had to reach out to the A/E firm to get a price for the design separate from the construction, and it is currently in the design phase | 2/13/26                 |
| P.002084       | Palmview ES                 | Change in the delivery method                                                                                                                                                                                                                                                                        | 2/14/2026               |
| P.002133       | Cooper City HS              | Poor contractor performance.                                                                                                                                                                                                                                                                         | 2/28/2026               |

# Schedule Milestones

The schools listed below are not anticipated to be completed\* by October 2025.

| Project Number | Project Name                           | Delay Event                                                                                                                                                                                                                                                                                           | *Substantial Completion |
|----------------|----------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| P.001824       | Lloyd Estates ES                       | A/E stopped working due to litigation issues. A/E omissions need to be redesigned.                                                                                                                                                                                                                    | 3/1/2026                |
| P.001818-HV2   | Charles Drew ES                        | The project was carved out, and it took a long time to get quotes from CSMPs for a design-build. We received some proposals, but the cost would be double. We had to reach out to the A/E firm to get a price for the design separate from the construction, and it is currently in the design phase. | 3/6/2026                |
| P.001796-ADA   | Atlantic West ES                       | The project was carved out, and the proposals came in too high. Therefore, it was decided that the architectural design would be done by the pre-construction team. A commitment was made to secure an MEP contract.                                                                                  | 3/7/2026                |
| P.001801-ADA   | Lauderhill 6-12 STEM-MED Magnet School | The project was carved out, and the proposals came in too high. Therefore, it was decided that the architectural design would be done by the pre-construction team. The 100% design revisions are being prepared to submit to the building department.                                                | 3/18/2026               |
| P.001801-FA1   | Lauderhill 6-12 STEM-MED Magnet School | Project manager requested A/E to be terminated for convenience. Scope of Work was carved out to be completed by a CSMP contractor.                                                                                                                                                                    | 4/1/2026                |
| P.002060       | Sheridan Technical Center              | The cost for the temp cooling has already been included in the GMP and approved by the Board, but it did cause a delay.                                                                                                                                                                               | 7/2/2026                |
| P.001638-ADA   | Broadview ES                           | The project was carved out, and the proposals came in too high. Therefore, it was decided that the architectural design would be done by the pre-construction team. The 100% design revisions are being prepared to submit to the building department.                                                | 8/28/2026               |

# Schedule Milestones

The schools listed below are not anticipated to be completed\* by October 2025.

| Project Number | Project Name                                  | Delay Event                                                                                                                                                                                                                                                   | *Substantial Completion |
|----------------|-----------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
| P.001900-FSP   | William E. Dandy MS                           | De-scope was approved and has been assigned to a CSMP contractor for design build.                                                                                                                                                                            | 8/28/2026               |
| P.000415       | Atlantic Technical College & Technical HS     | Design delays and change in delivery method                                                                                                                                                                                                                   | 10/30/2026              |
| P.001801-HVC   | Lauderhill 6-12 STEM-MED Magnet School - HVAC | The project is in procurement.                                                                                                                                                                                                                                | 10/31/2026              |
| P.001729-ADA   | Plantation MS - ADA Restrooms                 | The project was carved out, and the proposals came in too high. Therefore, it was decided that the architectural design would be done by the pre-construction team. The 100% design revisions are being prepared to submit to the building department.        | 10/31/2026              |
| P.001820       | Deerfield Beach ES                            | Due to the de-scoping of Building 1, the contractor refused to complete the project, leading us to decide to terminate his contract. Additionally, the A/E firm is no longer in business, which impedes the issuance of an ASI to de-scope the remaining work | 11/8/2026               |

**\*Completed projects:** Projects where the space has obtained occupancy and is being utilized for its intended use.

**\*\* On Hold Projects:** Projects are on hold. Preliminary planning will initiate once further decisions are made. These projects have been taken out of the SMART Program and placed in the Long-Range Planning process due to their scope and complexity.

Facilities

# Big 3 Status



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

# BLANCHE ELY HIGH SCHOOL



## PRIMARY RENOVATIONS


### ACTIVE CONSTRUCTION

BEFORE

AFTER



SCIENCE LAB



OUTDOOR DINING AREA



AWNING AND RAMP



BEFORE



AFTER



### STATUS OF WORK

- All scope is complete for all buildings. Final inspections are underway.

| BUILDING                        | STATUS   |
|---------------------------------|----------|
| 1, 2, 4, 10, 11, 13-18, 20 & 21 | Complete |



### OPEN CHANGE ORDERS

| BUILDING   | COMPLETION                  |
|------------|-----------------------------|
| Bldg 1     | New ADA Access              |
| Bldg 14-17 | An aluminum covered walkway |

# NORTHEAST HIGH SCHOOL



## PRIMARY RENOVATIONS

### ACTIVE CONSTRUCTION

BEFORE

AFTER




ROOFING



ADA RESTROOMS



WEIGHT ROOM



BEFORE

AFTER



### STATUS OF WORK

| BUILDING | STATUS                                                                                       |
|----------|----------------------------------------------------------------------------------------------|
| 1        | Fire Alarm and Fire Sprinkler completion pending shop drawing approval.                      |
| 2        | Complete                                                                                     |
| 3        | Complete                                                                                     |
| 4        | Smoke Vents replacement pending executed change order.                                       |
| 5        | Revised Schematic Designs for new AHU is on the Building Department for review and approval. |
| 6        | Complete                                                                                     |
| 7        | Complete                                                                                     |
| 12       | Complete                                                                                     |
| 15       | Complete                                                                                     |
| 17       | Complete                                                                                     |
| 25       | Complete                                                                                     |
| 85       | Complete                                                                                     |
| 86       | Complete                                                                                     |

# NORTHEAST HIGH SCHOOL (Continued)



## PRIMARY RENOVATIONS

ACTIVE CONSTRUCTION



## OPEN CHANGE ORDERS

| LOCATION                                                  |
|-----------------------------------------------------------|
| Covered Walkway Fire Sprinkler Piping                     |
| Building 2 – Roof Structural Repairs                      |
| Building 4 – Smoke Vent Replacements                      |
| Building 5 – Mechanical Mezzanine Completion              |
| Building 7 – Expansion Joints, Refurbishing Ceiling Joist |

# NORTHEAST HIGH SCHOOL (Continued)



## NEW CLASSROOM ADDITION

ACTIVE CONSTRUCTION



### STATUS OF WORK

| BUILDING                                     | STATUS                                                                                                                                |
|----------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|
| 7                                            | RTU installation completed                                                                                                            |
| 12                                           | ASI for F/S installation is approved by the Building Department. Contractor will commence work once their shop drawings are approved. |
| 29                                           | New Building are now occupied.                                                                                                        |
| 30                                           | New Building are now occupied.                                                                                                        |
| Demolition of Buildings<br>8, 9, 10, 11 & 27 | Demolition is completed, field pending sod installation.                                                                              |



### OPEN CHANGE ORDERS

| LOCATION                                  |
|-------------------------------------------|
| Building 8-11 irrigation connection       |
| Extended CA services                      |
| Fire Protection installation for Bldg. 12 |

# STRANAHAN HIGH SCHOOL



## PRIMARY RENOVATIONS


### ACTIVE CONSTRUCTION

BEFORE



ROOFING

AFTER



STEM LAB



MEDIA CENTER



BEFORE



AFTER



### STATUS OF WORK

| BUILDING | STATUS                                                                   |
|----------|--------------------------------------------------------------------------|
| 1        | Complete                                                                 |
| 2        | Complete                                                                 |
| 3        | Complete                                                                 |
| 4        | Complete                                                                 |
| 5        | Complete                                                                 |
| 6        | The work requested in the change order to the kiln room is 99% complete. |
| 7        | Complete                                                                 |
| 8        | Complete                                                                 |
| 9        | Complete                                                                 |
| 10 – 12  | Complete                                                                 |
| 13       | Complete                                                                 |
| 14       | Complete                                                                 |
| 15       | Complete                                                                 |
| 17       | Castaldi report completed – demolition recommended                       |
| 18       | Engineering report in progress – structural issues                       |
| 20       | Complete                                                                 |
| 21 – 23  | Complete                                                                 |

Facilities

# Actions Taken by the District to Reduce/Minimize Design and Construction Delays



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM




Established 1915  
**BROWARD**  
County Public Schools

# Change Order: Policy 8000

|               |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
|---------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Rule 1</b> | The Superintendent is authorized to approve all change orders up to \$5,000, based on the recommendation of the District's Program Management Organization and provided the cumulative total of all change orders for a specific project has not reached the cumulative limits identified in Rule 3 below.                                                                                                                                                                                                            |
| <b>Rule 2</b> | The Superintendent is authorized to approve change orders above \$5,000 and up to \$100,000, provided the cumulative total of all change orders for a specific project has not reached the cumulative limits identified in Rule 3 below. All change orders above \$5,000 will be reviewed by the District's Change Order Review Panel (CORP) and a recommendation will be provided to the Chief Facilities Officer prior to any authorization by the Superintendent.                                                  |
| <b>Rule 3</b> | Cumulative Limits – The cumulative limit of authority shall be 3 percent of the board approved construction contract amount up to a maximum of \$500,000. When the cumulative total of all change orders on a project has exceeded the ceiling established above, all subsequent change orders will require prior Board approval, except in emergency cases as declared by the Superintendent, or where the change order in question would be in the form of a credit, thereby reducing the Adjusted Contract amount. |
| <b>Rule 4</b> | Subsequent to approval of change orders by the Superintendent in accordance with Rules 1 and 2, notice shall be provided to the Board in a weekly report, outlining such approvals. Although all change orders will be confirmed by the Board at project closeout, this does not preclude change orders outlined in Rule 3 above from requiring prior Board approval.                                                                                                                                                 |

# Cumulative Change Orders (To-Date and This Quarter)

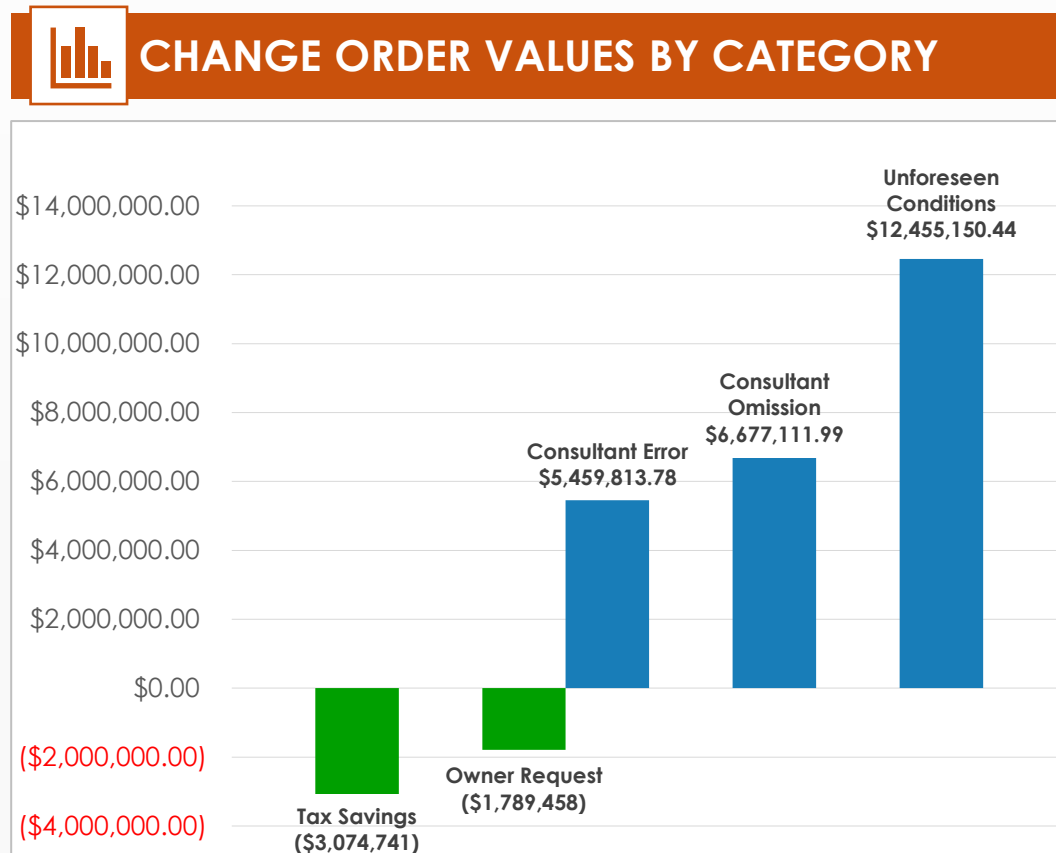

  
**\$966,577**  
Grand Total

  
**0.082%**  
Average Percent Change

| REASON                  | QUARTER CHANGE ORDER AMOUNT | AVERAGE PERCENT CHANGE |
|-------------------------|-----------------------------|------------------------|
| Tax Savings             | -830,139                    | -0.071%                |
| Owner Request           | -324,365                    | -0.028%                |
| Consultant Error        | 493,011                     | 0.042%                 |
| Consultant Omission     | 241,349                     | 0.021%                 |
| Unforeseen Condition    | 1,386,722                   | 0.118%                 |
| <b>QUARTERLY TOTALS</b> | <b>\$966,577</b>            | <b>0.082%</b>          |

# AECOM S/M/WBE Reporting

## AECOM December 2024 S/M/WBE Participation Reporting

|                                                      |               |
|------------------------------------------------------|---------------|
| Invoices Submitted to Client through December 2024*  | \$96,618,416  |
| Overall Paid to AECOM Paid through December 2024*    | \$90,438,628  |
| Paid on Prime Only Invoices through December 2024*   | \$22,103,750  |
| Non-S/M/WBE Subconsultant Paid through December 2024 | \$27,340,308  |
| S/M/WBE Subconsultant Paid through December 2024     | \$40,994,097  |
| <b>S/M/WBE Participation</b>                         | <b>45.33%</b> |



AECOM has invoiced through December 2024



AECOM and its sub-consultants have been paid for invoicing through December 2024

\* Excludes Additional Specialized Services

Facilities

# Assessment of Financial Risk



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915  
**BROWARD**  
County Public Schools

# Market Conditions and Risk Assessment

The December 2024 Risk Assessment has not changed from the September 2024 update. The summary is as follows:

| Date of Submittal | Risk Analysis Result Range (Percentage Increase / \$ increase in Millions) |                 |                      |
|-------------------|----------------------------------------------------------------------------|-----------------|----------------------|
|                   | Mid-Point Risk Result                                                      | 70% Risk Result | High End Risk Result |
| Jan 2017          | 22% / \$200                                                                | 26% / \$245     | 49% / \$439          |
| Dec 2018          | 46% / \$415                                                                | 48% / \$433     | 58% / \$528          |
| Jan 2020          | 47% / \$425                                                                | 49% / \$436     | 56% / \$507          |
| Jan 2021          | 55% / \$497                                                                | 56% / \$508     | 64% / \$575          |
| Dec 2021          | 64% / \$582                                                                | 65% / \$586     | 67% / \$603          |
| Mar 2022          | 77% / \$655                                                                | 77% / \$658     | 79% / \$676          |
| Jun 2022          | 81% / \$689                                                                | 81% / \$692     | 83% / \$706          |
| Sep 2022          | 81% / \$689                                                                | 81% / \$692     | 83% / \$706          |
| Dec 2022          | 82% / \$703                                                                | 83% / \$706     | 84% / \$717          |
| Mar 2023          | 84% / \$713                                                                | 84% / \$716     | 84% / \$727          |
| Jun 2023          | 85% / \$725                                                                | 85% / \$727     | 86% / \$736          |
| Sep 2023          | 84% / \$718                                                                | 84% / \$721     | 86% / \$733          |
| Dec 2023          | 84% / \$720                                                                | 85% / \$724     | 86% / \$738          |
| Mar 2024          | 85% / \$726                                                                | 86% / \$730     | 87% / \$741          |
| Jun 2024          | 85% / \$726                                                                | 85% / \$730     | 87% / \$741          |
| Sep 2024          | 85% / \$723                                                                | 85% / \$727     | 86% / \$738          |
| Dec 2024          | 84% / \$720                                                                | 85% / \$722     | 86% / \$733          |

Figure 1 - Risk Analysis Results Comparison

**NOTE:** The risk results include \$84.7M of scope that has been added to the SMART Program as described in more detail on Page 3.

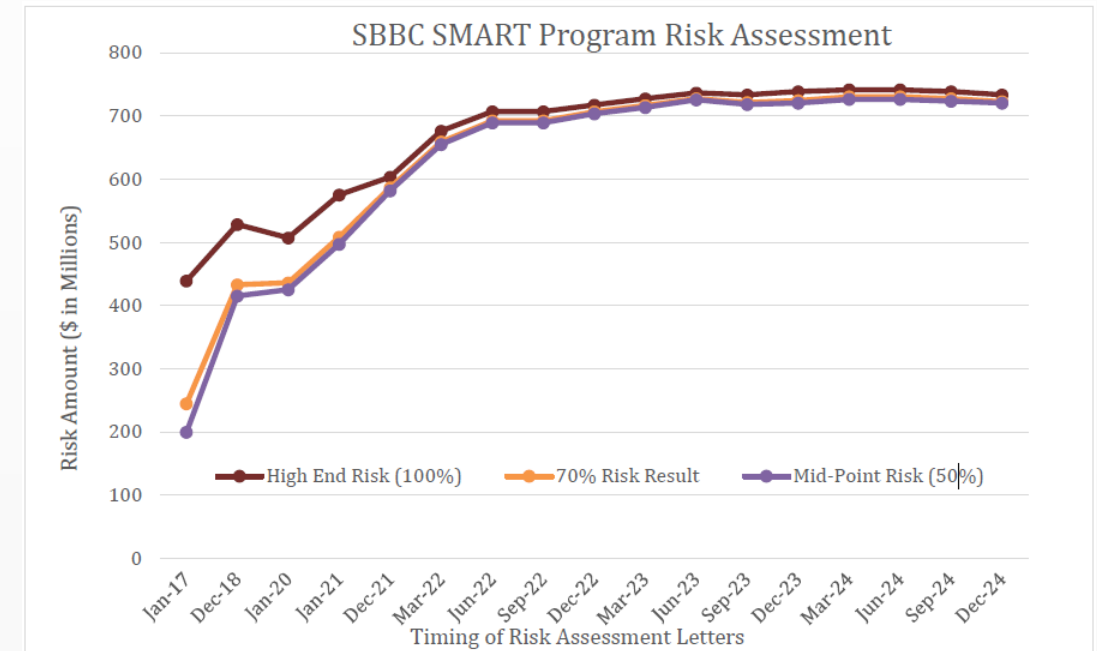


Figure 2 - Range of Potential Risk Outcomes Over Time

VOLUME OF  
CONSTRUCTION IN THE U.S.

TURNER CONSTRUCTION  
COST INDEX

CONSTRUCTION  
INFLATION



# Budget Activity



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915

**BROWARD**  
County Public Schools

# Budget Activity

## SMART Budget Summary




Year 1-11  
Current **SMART Budget**  
(millions)

**\$1,719.1**



SMART Program  
**BALANCE**  
(millions)


**\$136.5**

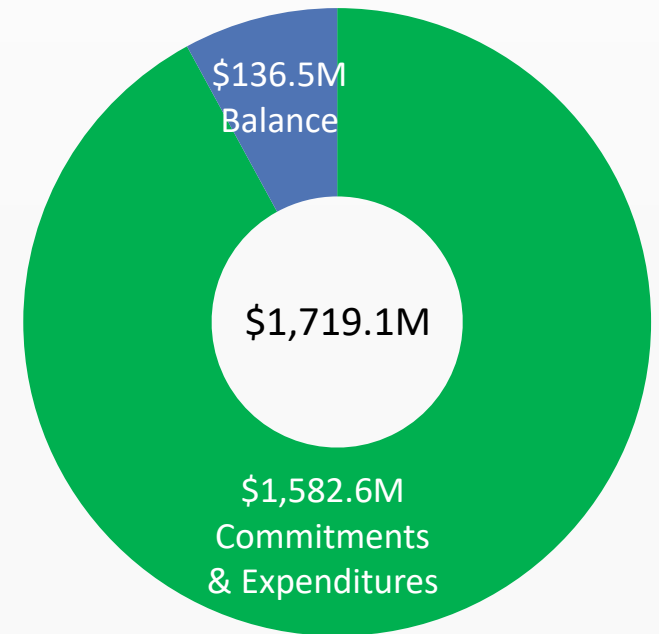

# Budget Activity


## SMART Budget Summary

**\$45.8 million  
expenditure  
increase from  
last quarter**



**Expenditures**  
thru FY25 Q2  
(millions)

**\$1,403.1**



**Purchase Orders** as of  
FY25 Q2  
(millions)

**\$179.6**

# Budget Activity

## SMART Program Closeout

### FINANCIAL CLOSEOUT


Financial Closeout is the point of the project where vendors have completed all work, all commitments have been paid and purchase orders are closed following the School Board approval of the final release of retainage and final acceptance of the project.

As of December 31, 2024, the savings for all Safety, Music & Art, Athletics, Renovations, and Technology (SMART) projects is approximately **\$23 million**.

- Approximately \$13 million of these savings occurred in Music & Art, Athletics, and Technology projects and the remaining \$10 million in Primary Renovation projects.
- The District will continue financially close out Primary Renovation projects until the anticipated SMART Program completion date of October 2025.



**19% of SMART Program primary renovation projects have been financially closed out resulting in approximately \$10M in savings.**

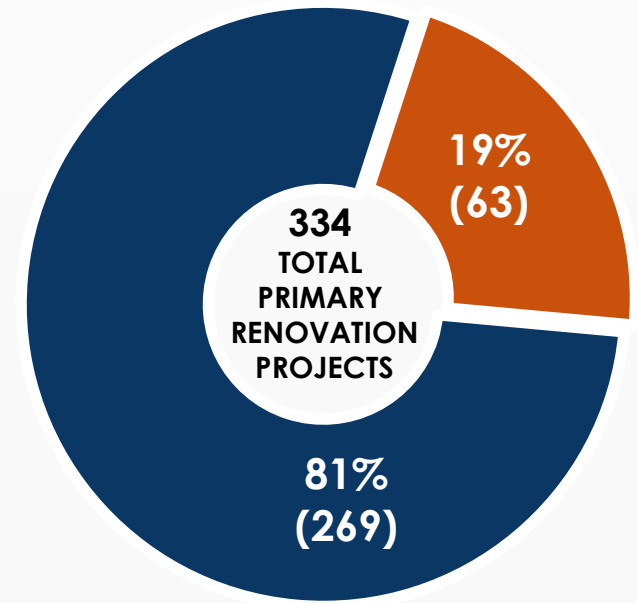

# Economic Development & Diversity Compliance

## Supplier Diversity Outreach Program



# CERTIFICATION INDUSTRY CATEGORIES

## By Ethnicity and Gender

| Certified Firms<br>by Ethnicity & Gender | FY25 Q1<br>Certified<br>Firms | FY25 Q2<br>Certified<br>Firms | Construction | Architecture<br>& Engineering | Professional<br>Services | Goods     | Other<br>Services |
|------------------------------------------|-------------------------------|-------------------------------|--------------|-------------------------------|--------------------------|-----------|-------------------|
| African American Male                    | 145                           | 150                           | 57           | 8                             | 19                       | 13        | 53                |
| African American Female                  | 129                           | 135                           | 26           | 1                             | 26                       | 12        | 70                |
| Asian American Male                      | 20                            | 20                            | 1            | 7                             | 1                        | 2         | 9                 |
| Asian American Female                    | 11                            | 13                            | 4            | 2                             | 3                        | 1         | 3                 |
| Hispanic American Male                   | 132                           | 140                           | 68           | 19                            | 6                        | 12        | 35                |
| Hispanic American Female                 | 118                           | 125                           | 49           | 10                            | 11                       | 18        | 37                |
| Veteran Business Enterprise Male         | 1                             | 1                             | 0            | 0                             | 0                        | 1         | 0                 |
| Veteran Business Enterprise Female       | 1                             | 1                             | 0            | 0                             | 0                        | 0         | 1                 |
| Caucasian Female (WBE)                   | 104                           | 108                           | 37           | 7                             | 19                       | 7         | 38                |
| Non-Minority Male (SBE)                  | 68                            | 72                            | 33           | 9                             | 6                        | 9         | 15                |
| <b>Total</b>                             | <b>729</b>                    | <b>765</b>                    | <b>275</b>   | <b>63</b>                     | <b>91</b>                | <b>75</b> | <b>261</b>        |
| Male-owned Certified Firms               | 366                           | 383                           | 159          | 43                            | 32                       | 37        | 112               |
| Female-owned Certified Firms             | 363                           | 382                           | 116          | 20                            | 59                       | 38        | 149               |

Notes:

<sup>1</sup>Certified firms may be categorized under multiple industry categories.

# Economic Development & Diversity Compliance Commitment & Spend Analysis

| SMART CONTRACTS ACTUAL SPEND     |                                                              |                                           |                                             |                                                                        |                |
|----------------------------------|--------------------------------------------------------------|-------------------------------------------|---------------------------------------------|------------------------------------------------------------------------|----------------|
| By Ethnicity & Gender            | Certified Prime Spend Total (FY15 Q2 - FY25 Q2) <sup>1</sup> | Cumulative Spend % Based on Overall Total | Cumulative Spend % Based on Certified Total | Sub Contractor/Consultant Commitments <sup>2</sup> (FY22 Q4 – FY24 Q4) |                |
| African American-owned           | \$74,867,500.47                                              | 3.96%                                     | 13.70%                                      | \$18,093,979.97                                                        | 14.33%         |
| Hispanic American-owned          | \$416,974,524.58                                             | 22.07%                                    | 76.28%                                      | \$66,326,481.99                                                        | 52.54%         |
| Asian American-owned             | \$13,767,437.56                                              | 0.73%                                     | 2.52%                                       | \$0.00                                                                 | 0.00%          |
| Native American-owned            | \$0.00                                                       | 0.00%                                     | 0.00%                                       | \$0.00                                                                 | 0.00%          |
| White Female (WBE)               | \$33,390,540.96                                              | 1.77%                                     | 6.11%                                       | \$25,472,303.71                                                        | 20.18%         |
| Non-Minority Male (SBE)          | \$7,637,466.65                                               | 0.40%                                     | 1.40%                                       | \$16,355,379.75                                                        | 12.95%         |
| <b>Total Certified Spend</b>     | <b>\$546,637,470.22</b>                                      | <b>28.93%</b>                             | <b>100.00%</b>                              | <b>\$126,248,145.41</b>                                                | <b>100.00%</b> |
| <b>Total Non-Certified Spend</b> | <b>\$1,342,768,209.19</b>                                    | <b>71.07%</b>                             |                                             |                                                                        |                |
| <b>Total Spend</b>               | <b>\$1,889,405,679.41</b>                                    | <b>100.00%</b>                            |                                             |                                                                        |                |

Notes:

<sup>1</sup> Source: BCPS Capital Budget Department

<sup>2</sup> Tracking of Sub Commitment data began in FY22 Q4.

# VALUE OF PURCHASE ORDERS TO E/S/M/WBE FIRMS PER SMART CATEGORY FY25 Q1

|  |  |  |  |  |
|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|
| S                                                                                 | M                                                                                 | A                                                                                   | R                                                                                   | T                                                                                   |
| SAFETY                                                                            | MUSIC + ART                                                                       | ATHLETICS                                                                           | RENOVATION                                                                          | TECHNOLOGY                                                                          |
| \$18,238,290.56                                                                   | \$ 0                                                                              | \$12,699.00                                                                         | \$528,386,480.66                                                                    | \$ 0                                                                                |

**TOTAL CUMULATIVE COMMITMENT & SPEND: \$546,637,470.22**

*Note: Source data provided by BCPS Capital Budget Department.*

# Economic Development & Diversity Compliance Marketing & Outreach



## FY25 Q1 ACTIVITIES

|                        |                                  |                                 |
|------------------------|----------------------------------|---------------------------------|
| 864                    | 204                              | 1333                            |
| EDDC Concierge Service | Community & Stakeholder Meetings | One-on-One Technical Assistance |

## FY25 Q2 ACTIVITIES

|                        |                                  |                                 |
|------------------------|----------------------------------|---------------------------------|
| 404                    | 94                               | 1483                            |
| EDDC Concierge Service | Community & Stakeholder Meetings | One-on-One Technical Assistance |

## EDDC HOSTED EVENTS & TRAINING

| Date                                              | Events                                                                         | In-Person Attendees | Virtual Attendees | Total Attendees |
|---------------------------------------------------|--------------------------------------------------------------------------------|---------------------|-------------------|-----------------|
| <b>Outreach Events</b>                            |                                                                                |                     |                   |                 |
| Nov. 13, 2024                                     | Brunch & Learn: Veterans Business Initiative                                   | 89                  | N/A               | 89              |
| Dec. 4, 2024                                      | Brunch & Learn: CORE Construction                                              | 173                 | N/A               | 173             |
| Subtotal                                          |                                                                                | 262                 | 0                 | 262             |
| <b>2024 Inaugural Business Excellence Program</b> |                                                                                |                     |                   |                 |
| Oct. 17, 2024                                     | Business Basics Bootcamp: Mastering the Fundamentals                           | 329                 | N/A               | 329             |
| Oct. 24, 2024                                     | State of Small Business Funding                                                | 185                 | N/A               | 185             |
| Oct. 31, 2024                                     | Legal Launchpad: Essential Foundations for Business Success                    | N/A                 | 208               | 208             |
| Nov. 7, 2024                                      | Bond Boost: Elevate Your Business to Bond-Ready Status!                        | 137                 | N/A               | 137             |
| Nov. 14, 2024                                     | Fuel Business Growth: Accessing Non-Competitive Opportunities Under \$50K      | 162                 | N/A               | 162             |
| Nov. 21, 2024                                     | Trailblazer Talks: Acquire Insights and Learn Strategies from Industry Leaders | 337                 | N/A               | 337             |
| Dec. 5, 2024                                      | Graduation Affair: Celebrating Your Journey to Excellence                      | 258                 | N/A               | 258             |
| Subtotal                                          |                                                                                | 1408                | 208               | 1616            |
| Total Attendees                                   |                                                                                | 1670                | 208               | 1878            |

# Economic Development & Diversity Compliance

## Marketing & Outreach Continued

### EDDC QUARTERLY NEWSLETTER - ON POINT WITH EDDC

EDDC's quarterly newsletter is designed to inform the community of news, events, procurement opportunities, and departmental accomplishments.



Volume 2, Issue 2 | FY25 Q2  
October 2024 – December 2024

Economic Development & Diversity Compliance Department

### Black History Month 2025: African Americans and Labor

As we celebrate Black History Month, February 2025, the Economic Development & Diversity Compliance Department honors the generations of African American entrepreneurs, business leaders, and innovators who have shaped our nation's economy with such profound contributions.

The legacy continues through the District's commitment to foster opportunities for economic growth, community connections, and strategic partnership for small, local firms to expand and endure. We encourage your support of Certified firms through the EDDC #buybroward initiative, using the EDDC Inaugural Broward Business Directory available online at [www.Browardschools.com/EDDC](http://www.Browardschools.com/EDDC).





### LEVEL UP WITH ARTIFICIAL INTELLIGENCE

Artificial Intelligence (AI) is no longer the future — it is the present and can transform your business. How can you win with AI? Save time, cut costs, automate tasks, and more with AI. Here's a great introductory article to begin:

**AI for Small Business 101: How to Get Started**  
[www.uschamber.com/co/run/technology/small-business-ai-guide](http://www.uschamber.com/co/run/technology/small-business-ai-guide)

 *Economic development and job creation are the only real solutions to poverty.* - Earvin "Magic" Johnson



Superintendent Howard Hepburn, Darrell Hardge, and James Knapp, BEF CEO

### CONGRATULATIONS

EDDC salutes Darrell Hardge, aka "Mr. Hardge the EduTainer" as the Broward Education Foundation (BEF) 2024 Hall of Fame Distinguished Alumni Education Award recipient. A graduate of the Boyd Anderson High School Class of '87, Mr. Hardge is President of *New Dimension International Training & Consulting*, a BCPS Certified Small/Minority Business Enterprise.

Mr. Hardge is an author, motivational teacher, and youth advocate. His *Life Is What You Make It Empowerment Seminars* encourage students to become responsible for their lives and equips them with skills, strategies, and information needed to create the life they desire.

[WWW.BROWARDSCHOOLS.COM/EDDC](http://WWW.BROWARDSCHOOLS.COM/EDDC) | 754.321.0770

# Economic Development & Diversity Compliance

## Marketing & Outreach Continued

### 2024 INAUGURAL BUSINESS EXCELLENCE PROGRAM GRADUATION *ELEVATE, EMPOWER, CONNECT: A JOURNEY OF GROWTH AND IMPACT*

- ✓ 800 Small and aspiring business owners in attendance
- ✓ 258 Graduates
- ✓ 40 Public and private sector subject matter expert panelists
- ✓ Graduation Emcee: Kirk Gimenez, Founder and Host of *Xizzle TV*
- ✓ Keynote Address: Dr. Marcus Bright, Educator, Author, and Social Impact Leader.
- ✓ Special Remarks: Dr. Howard Hepburn, Superintendent of Schools

Sessions covered the following themes:

- Business fundamentals and funding
- Critical legal insights
- Bonding for large opportunities
- Fueling growth with opportunities under \$50K
- Building strategic collaborations
- AI Technology for innovation and growth



# Economic Development & Diversity Compliance

## Marketing & Outreach Continued



View the event  
recap video.



# Economic Development & Diversity Compliance

## Social Media Presence

**STAY CONNECTED | STAY INFORMED**

---



[@BCPSEDDC](https://twitter.com/BCPSEDDC)



[BROWARD SCHOOLS EDDC](https://www.facebook.com/BrowardSchoolsEDDC)



[@BCPSEDDC](https://www.youtube.com/BCPSEDDC)



[BCPSEDDC](https://www.instagram.com/BCPSEDDC)

# Communications Updates



BCPS\_SMART



BCPSSMART



BCPS SMART FUTURES



BCPSSMARTFUTURES.COM



Established 1915

**BROWARD**  
County Public Schools

# Quarterly Results Overview

## MILESTONES

WINTER CONSTRUCTION

FOUR RIBBON-CUTTING CEREMONIES

JAMES S. RICKARDS MIDDLE SCHOOL TOPPING OUT CELEBRATION

## MULTIFACETED OUTREACH

KEEPING THE COMMUNITY INFORMED

SMALL BUSINESS OUTREACH: ECONOMIC DEVELOPMENT & DIVERSITY COMPLIANCE

INFORMING THROUGH SOCIAL MEDIA

## QUARTER RESULTS OVERVIEW

29

SCHOOL VISITS

4

MEDIA MENTIONS

5.7K

WEBSITE VISITORS

9.1k

PAGE VIEWS

## SOCIAL MEDIA PERFORMANCE



@BCPS\_SMART

1,343

FOLLOWERS

21

POSTS

132,152

IMPRESSIONS



BCPSSMART

563

FOLLOWERS

18

POSTS

1,569

IMPRESSIONS



@BCPS\_SMART

1,139

FOLLOWERS

17

POSTS

2,999

IMPRESSIONS

# Winter Construction

Though classrooms fall quiet during winter break, SMART Program construction sites buzz with activity. The SMART Communications team took advantage of this time to highlight the hard work and progress achieved by the construction team while students were out. The team visited these sites during winter break to gather visual content that showcased the remarkable advancements made at various schools.

## A few of our visits included:

- Coconut Creek High School
- Deerfield Beach High School
- Driftwood Middle School
- Flamingo Elementary School
- McArthur High School
- McFatter Technical College & High School
- Nova High School
- Nova Middle School
- Park Springs Elementary School
- Peters Elementary School
- Plantation High School
- Plantation Middle School
- Silver Lakes Middle School
- South Broward High School



# Celebrating Milestones

Ribbon-cutting ceremonies highlight the SMART Bond Program's dedication to enhancing educational facilities in Broward County.



## DEERFIELD BEACH HIGH SCHOOL MEDIA CENTER RIBBON-CUTTING CEREMONY

**CEREMONY DATE: OCTOBER 24, 2024**

On October 23, 2024, Deerfield Beach High School unveiled its new media center. Notable figures such as School Board Vice-Chair Debra Hixon (Countywide At-Large Seat 9), School Board Member Nora Rupert (District 7), Superintendent Dr. Hepburn, District leadership and staff, as well as representatives from the city's Education Advisory Board and SMART Program, were all in attendance. Members of the school community, including the principal, teachers, and students, also participated.



View the  
event video  
and read the  
blog recap.



## SHERIDAN TECHNICAL COLLEGE MEDIA CENTER RIBBON-CUTTING CEREMONY

**CEREMONY DATE: OCTOBER 25, 2024**

On October 25, 2024, Sheridan Technical College held a ribbon-cutting ceremony to unveil its new media center. The ceremony welcomed a range of District leadership and community figures, including School Board Vice-Chair Debra Hixon (Countywide At-Large Seat 9), School Board Members Daniel P. Foganholi (District 1), Sarah Leonardi (District 3), Superintendent Dr. Hepburn, and other District staff.



View the  
event recap  
video.



# Celebrating Milestones

Ribbon-cutting ceremonies highlight the SMART Bond Program's dedication to enhancing educational facilities in Broward County.



**CEREMONY DATE: NOVEMBER 15, 2024**

On November 15, 2024, Margate Elementary School unveiled its new classroom building and playcourt. Notable figures were in attendance, including School Board Vice-Chair Debra Hixon (Countywide At-Large Seat 9), School Board Member Lori Alhadeff (District 4), School Board Member Nora Rupert (District 7), and Superintendent Dr. Howard Hepburn, as well as District leadership and staff. Members of the school community, including the principal, teachers, and students, also participated.



**CEREMONY DATE: DECEMBER 12, 2024**



On December 12, 2024, Riverside Elementary School unveiled its new media center. Notable figures were in attendance, including School Board Chair Debra Hixon (Countywide At-Large Seat 9), School Board Member Lori Alhadeff (District 4), and Superintendent Dr. Howard Hepburn, as well as District leadership and staff. Members of the school community, including the principal, teachers, and students, also participated.



View the  
event recap  
video.



# Celebrating Milestones

Topping Out is a significant milestone within the SMART Bond Program's construction journey, marking the placement of the last structural beam on a new building.



## JAMES S. RICKARDS MIDDLE SCHOOL TOPPING OUT CELEBRATION

**CEREMONY DATE: NOVEMBER 21, 2024**

On November 21, 2024, James S. Rickards Middle School held a topping out celebration. A topping out celebration is traditionally held when the last beam in construction is placed at the top of the structure. The event featured delicious food and refreshments for all project staff to enjoy. The principal, school staff, and other members of the community were all in attendance.



View the  
event recap  
video.



# Keeping The Community Informed

The SMART Communications team aims to maintain transparency with the community. To achieve this goal during the current quarter, the team increased school site visits, issued multiple blog posts, and provided consistent updates on social media.

4

## MEDIA MENTIONS THIS QUARTER

The SMART Bond Program continues to garner significant media attention, highlighting its ongoing impact on Broward County's educational landscape. Key highlights from recent coverage include:

- **Riverside Elementary School's** new \$450,000 media center unveiling, covered by local outlets like **Coral Springs Talk** and **TAPinto Coral Springs**.
- **Deerfield Beach High School's** \$1 million investment in campus renovations, reported by **WSVN 7 News**.
- **Margate Elementary School's** ongoing \$9,019,680 construction project, featured in the **Margate News**.



MargateNews.net



29

## SCHOOL VISITS THIS QUARTER

The SMART Communications team increased school visits this quarter to capture the captivating transformations occurring at schools district-wide. This quarter, 29 schools were visited to capture photos and videos showcasing the ongoing progress of the SMART program. Additionally, each school visited had their SMART Program webpages updated to keep the public informed.

2

## BLOG POSTS THIS QUARTER

The SMART Communications team published two blog posts this quarter. One post showcased the media center ribbon-cutting ceremony at Deerfield Beach High School, while the other post announced the commencement of Winter Construction. The posts on the SMART Program website play a crucial role in communicating and celebrating the latest achievements of the SMART Program.



Read the latest SMART Program updates.

# Multifaceted Outreach



## SMALL BUSINESS OUTREACH – ECONOMIC DEVELOPMENT AND DIVERSITY COMPLIANCE ELEVATE, EMPOWER, CONNECT

During this quarter, the Economic Development & Diversity Compliance (EDDC) department continued their Business Excellence Program with a six-part class series to help small businesses work with Broward schools and improve their performance in critical areas. The SMART Communications team assisted the EDDC's Business Excellence Program with event photography and videography. Additionally, the SMART Communications team provided graphic design services, which included the creation of flyers, a graduation booklet, social media templates, and additional materials.

- **10/17/2024** – Business Basics Bootcamp: Mastering the Fundamentals
- **10/24/2024** – State of Small Funding
- **11/7/2024** – Bond Boost: Elevate your Business to Bond-Ready status
- **11/7/2024** – Fast Track to Payment: Mastering the Local Government Invoicing Process
- **11/21/2024** – Trailblazer Talks: Acquire Insights and Learn Strategies from Industry Leaders
- **12/5/2024** – A Graduation Affair: Celebrating your Journey to Excellence



# Informing Through Social Media

This quarter, the SMART Communications team published **141 social media posts** to over **3,045 followers** across three social media platforms. These posts highlight SMART Program updates at Broward County Public Schools with recent photos and information to keep the public informed.



## TOP POSTS ON FACEBOOK


| BCPS SMART Futures<br>Tue 11/19/2024 8:49 am EST                                          |    |
|-------------------------------------------------------------------------------------------|----|
| We enjoyed celebrating Sheridan Technical College & High School's brand-new media center. |    |
|                                                                                           |    |
| Total Engagements                                                                         | 16 |
| Reactions                                                                                 | 6  |
| Comments                                                                                  | 0  |
| Shares                                                                                    | 3  |
| Post Link Clicks                                                                          | —  |
| Other Post Clicks                                                                         | 7  |

| BCPS SMART Futures<br>Mon 11/25/2024 9:14 am EST                                                             |   |
|--------------------------------------------------------------------------------------------------------------|---|
| Coral Springs Middle is looking and feeling fresh, thanks to new gym lighting and two new air handler units. |   |
|                                                                                                              |   |
| Total Engagements                                                                                            | 6 |
| Reactions                                                                                                    | 2 |
| Comments                                                                                                     | 0 |
| Shares                                                                                                       | 0 |
| Post Link Clicks                                                                                             | — |
| Other Post Clicks                                                                                            | 4 |

| BCPS SMART Futures<br>Thu 10/31/2024 1:50 pm EDT                                                                       |   |
|------------------------------------------------------------------------------------------------------------------------|---|
| Last week, we celebrated the completion of Deerfield Beach High School's media center! 🎉 We look forward to hearing... |   |
|                                                                                                                        |   |
| Total Engagements                                                                                                      | 6 |
| Reactions                                                                                                              | 2 |
| Comments                                                                                                               | 0 |
| Shares                                                                                                                 | 0 |
| Post Link Clicks                                                                                                       | — |
| Other Post Clicks                                                                                                      | 4 |

# Informing Through Social Media

## TOP POSTS ON INSTAGRAM

|                                                                                                                                  |            |
|----------------------------------------------------------------------------------------------------------------------------------|------------|
|  <b>bcps_smart</b><br>Tue 11/19/2024 1:45 pm EST |            |
| We had an amazing time celebrating Sheridan Technical College & High School's brand-new media center.                            |            |
|                                                  |            |
| <b>Total Engagements</b>                                                                                                         | <b>141</b> |
| Likes                                                                                                                            | 78         |
| Comments                                                                                                                         | 16         |
| Shares                                                                                                                           | 45         |
| Saves                                                                                                                            | 2          |

|                                                                                                                                   |            |
|-----------------------------------------------------------------------------------------------------------------------------------|------------|
|  <b>bcps_smart</b><br>Wed 10/23/2024 7:30 pm EDT |            |
| A vibey morning celebrating Deerfield Beach High School's new media center 🎉                                                      |            |
|                                                  |            |
| <b>Total Engagements</b>                                                                                                          | <b>128</b> |
| Likes                                                                                                                             | 75         |
| Comments                                                                                                                          | 7          |
| Shares                                                                                                                            | 44         |
| Saves                                                                                                                             | 2          |

|                                                                                                                                   |           |
|-----------------------------------------------------------------------------------------------------------------------------------|-----------|
|  <b>bcps_smart</b><br>Fri 11/1/2024 10:15 am EDT |           |
| We had such a fantastic time celebrating the brand-new media center at Sheridan Technical College! The event was filled...        |           |
|                                                 |           |
| <b>Total Engagements</b>                                                                                                          | <b>19</b> |
| Likes                                                                                                                             | 19        |
| Comments                                                                                                                          | 0         |
| Saves                                                                                                                             | 0         |

## TOP POSTS ON X

|                                                                                                                                      |           |
|--------------------------------------------------------------------------------------------------------------------------------------|-----------|
|  <b>@BCPS_SMART</b><br>Tue 11/19/2024 1:16 pm EST |           |
| We had an amazing time celebrating Sheridan Technical College & High School's brand-new media center.                                |           |
|                                                   |           |
| <b>Total Engagements</b>                                                                                                             | <b>37</b> |
| Likes                                                                                                                                | 6         |
| @Replies                                                                                                                             | 0         |
| Reposts                                                                                                                              | 2         |
| Post Link Clicks                                                                                                                     | —         |
| Other Post Clicks                                                                                                                    | 29        |
| Other Engagements                                                                                                                    | 0         |


  

|                                                                                                                                      |           |
|--------------------------------------------------------------------------------------------------------------------------------------|-----------|
|  <b>@BCPS_SMART</b><br>Thu 11/21/2024 4:42 pm EST |           |
| The media center at Silver Lakes Middle School is looking brand new! With vibrant new paint and furniture, this space will...        |           |
|                                                   |           |
| <b>Total Engagements</b>                                                                                                             | <b>15</b> |
| Likes                                                                                                                                | 4         |
| @Replies                                                                                                                             | 0         |
| Reposts                                                                                                                              | 0         |
| Post Link Clicks                                                                                                                     | —         |
| Other Post Clicks                                                                                                                    | 11        |
| Other Engagements                                                                                                                    | 0         |

|                                                                                                                                       |           |
|---------------------------------------------------------------------------------------------------------------------------------------|-----------|
|  <b>@BCPS_SMART</b><br>Tue 11/12/2024 11:15 am EST |           |
| Take in the sights and sounds of Deerfield Beach High School Ribbon-Cutting 🎉                                                         |           |
|                                                    |           |
| <b>Total Engagements</b>                                                                                                              | <b>14</b> |
| Likes                                                                                                                                 | 0         |
| @Replies                                                                                                                              | 0         |
| Reposts                                                                                                                               | 0         |
| Post Link Clicks                                                                                                                      | —         |
| Other Post Clicks                                                                                                                     | 14        |
| Other Engagements                                                                                                                     | 0         |

# Stay Connected







**A RATED**  
SCHOOL DISTRICT

Established 1915  
**BROWARD**  
County Public Schools

**SAFETY  
MUSIC & ART  
ATHLETICS  
RENOVATION  
TECHNOLOGY**

**Questions &  
Answers**

# The School Board of Broward County Florida

Debra Hixon, Chair  
Sarah Leonardi, Vice-Chair

Lori Alhadeff  
Brenda Fam, Esq.  
Dr. Jeff Holness  
Maura McCarthy Bulman  
Nora Rupert  
Rebecca Thompson  
Dr. Allen Zeman

Dr. Howard Hepburn, Superintendent of Schools



The School Board of Broward County, Florida, prohibits any policy or procedure which results in discrimination on the basis of age, color, disability, gender identity, gender expression, genetic information, marital status, national origin, race, religion, sex or sexual orientation. The School Board also provides equal access to the Boy Scouts and other designated youth groups. Individuals who wish to file a discrimination and/or harassment complaint may call the Director, Equal Educational Opportunities/ADA Compliance Department & District's Equity Coordinator/Title IX at 754-321-2150 or Teletype Machine (TTY) 754-321-2158.

Individuals with disabilities requesting accommodations under the Americans with Disabilities Act Amendments Act of 2008 (ADAAA), may call Equal Educational Opportunities/ADA Compliance Department at 754-321-2150 or Teletype Machine (TTY) 754-321-2158
